STANLEY Access Technologies

ALLEGION
Part of the Allegion Family of Brands

PROJECT

PNC BANK

3501 VANDENBERG WAY

ESTERO, FL 33928-6601

CONTRACTOR / OWNER

PNC BANK

PO BOX 100044

PITTSBURGH, PA

BRANCH (INSTALLATION AND SERVICE)

ALLEGION ACCESS TECHNOLOGIES LLC
9838 Currie Davis Drive Tampa, FL 33619

Construction Manager : Sean Parry
Installation Coordinator :
Installation Phone Number :
Installation Fax Number :
Service Phone Number : 888-366-7444

TERRITORY MANAGER (SALES)

Territory Manager : Gregory Erickson
Sales Phone Number : 4806529593
Sales Fax Number :
Sales Email Address : gregory.erickson@allegion.com

RS&H

ATTENTION: THIS REVIEW IS LIMITED TO THE REQUIREMENTS OF THE CONTRACT FOR ARCHITECT/ENGINEER ACTION ON SUBMITTALS. REVIEW OF SUBMITTALS IS ONLY FOR CONFORMANCE WITH THE DESIGN CONCEPT OF THE PROJECT AND DOES NOT RELIEVE THE CONTRACTOR OF RESPONSIBILITY FOR ERRORS OR OMISSIONS IN SUBMITTALS. THE CONTRACTOR SHALL DETERMINE AND VERIFY ALL FIELD MEASUREMENTS, FIELD CONSTRUCTION CRITERIA, QUANTITIES, MATERIALS, CATALOG NUMBERS AND SIMILAR DATA, AND CHECK AND COORDINATE EACH SUBMITTAL WITH THE REQUIREMENTS OF THE WORK AND OF THE CONTRACT DOCUMENTS.

SUBMITTAL REVIEW DISPOSITION

☐ APPROVED
☐ APPROVED AS NOTED
☐ NOT APPROVED
☐ REVISE AND RESUBMIT
☐ RETURNED WITHOUT ACTION
☒ NO EXCEPTION TAKEN

BY: CurninJ DATE: 09/28/2026

Reviewed for design intent only.

Job Name:	PNC Bank - Estero, FL	**Job#:** Q-284899 **Date:** Aug 27 2026
Location:	3501 Vandenberg Way Estero, FL 33928-6601	**Product Qty:** 1.00
Door Location:	INTERIOR DOOR #100B	**Product:** D/G3000 SS

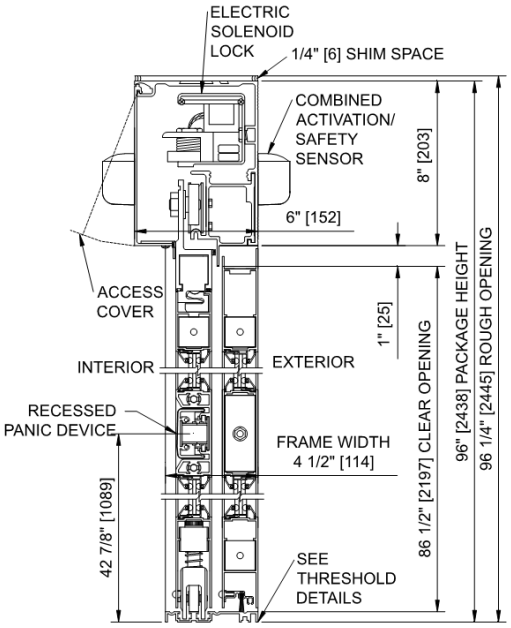

1 VERTICAL SECTION

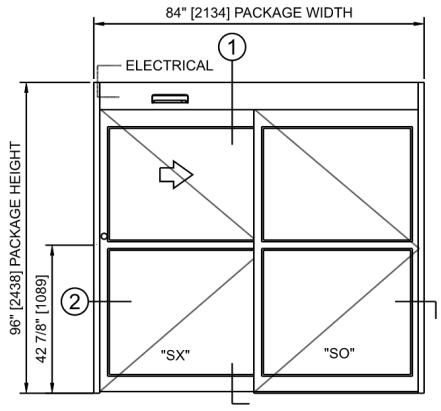

ELEVATION VIEW
VIEWED FROM BREAKOUT SIDE

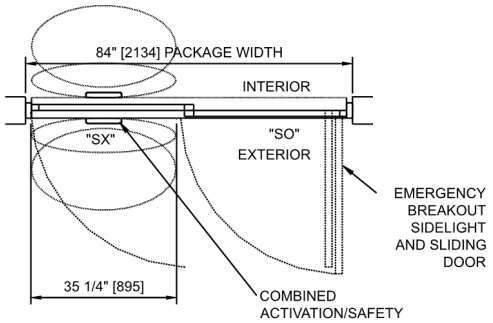

PLAN VIEW

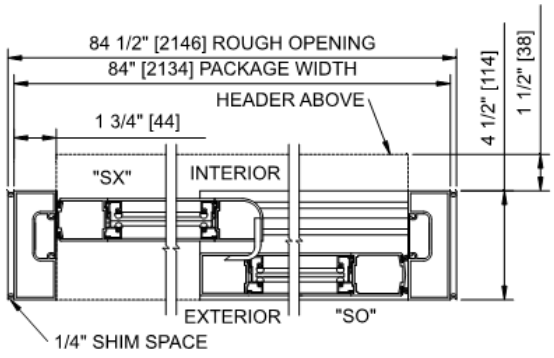

2 HORIZONTAL SECTION

STANLEY	**Job Name:** PNC Bank - Estero, FL **Location:** 3501 Vandenberg Way Estero, FL 33928-6601, {1} {2} **Door Location:** INTERIOR DOOR #100B	**Job#:** Q-284899 **Date:** Aug 27 2026 **Product Qty:** 1.00 **Product:** D/G3000 SS



BOTTOM RAIL, 10"
6063-T6



MUNTIN BAR, 4"
6063-T6



STILE, NARROW
6063-T6

Detail-Transom not Selected in the Package



PANEL GLAZING SECTIONS
1/4" GLASS



JAMB, 4 1/2"
6063-T6



FLAT EXTRUSION
UNDER "SO" PANEL ONLY

THRESHOLD-TAPERED EXTRUSION
4 1/2" FRAME

STANLEY

Job Name: PNC Bank - Estero, FL
Location: 3501 Vandenberg Way
Estero, FL 33928-6601
Door Location: INTERIOR DOOR #100B

Job#: Q-284899 **Date:** Aug 27 2026
Product Qty: 1.00
Product: D/G3000 SS

Door Details

Package Width	Masonry/Rough Opening Width	Clear Door Opening Width	Emergency Breakout	Package Height	Rough Opening Height
84.00	84.50	35.28	75.00	96.00	96.25

Options

Finish

COLOR OF DOOR PACKAGE	SPECIAL FINISH
TYPE OF SPECIAL FINISH	BLACK ANODIZE

Locking / Access Control

Lock Configuration Description	NO LOCK/CYLINDER/THUMBTURN
REC Access Control	Y
Solenoid Lock Description	FAIL SECURE

Options and Accessories

Hardware Color	BLACK
Switch and Control Options	KEYSWITCH - 6 POSITION,DOOR POSITION SWITCH,ALARM CONTACTS
Threshold Color	CLEAR ANODIZED THRESHOLD
Threshold Option	ANGLE/FLAT 5.25 (SO ONLY)

Glass Specifications

SO Glass Thickness	0.250 "
SX Glass Thickness	0.250 "

Inclusions/Exclusions

Inclusions
Door package installation.
Subcontractor for storefront work.
Glass & Glazing
Caulking

Exclusions
120 volts AC to inside auto door header 5 amp min.
Cleaning and protection of installed material.
Permits & Inspections.
Prevailing Wage and/or Certified Payroll.
Cleaning of installed materials.
Protection of installed materials.
Painting, patching & flooring work.
Preparation of rough opening.
Recess prep & grout for track or threshold.
Break metal
After hours premium labor
Back boxes & low voltage wiring from any control to inside auto door header.
Structural support / wood blocking for swing headers
Doors, frames & associated hardware.
Demolition of existing storefront.
Union Labor

Exclusion Note

Shop Drawing / Submittal Review

Date: 09/28/2026

☑ No Exceptions Taken ☐ Furnish With Changes Noted ☐ Review and Resubmit ☐ Rejected

SUBMITTAL WAS REVIEWED FOR GENERAL CONFORMANCE TO THE CONTRACT DOCUMENTS. THE GENERAL CONTRACTOR IS RESPONSIBLE FOR CONFIRMING AND CORRELATING DIMENSIONS AT JOBSITE FOR TOLERANCE, CLEARANCE, QUANTITIES, FABRICATION, TECHNIQUES OF CONTRUCTION, COORDINATION OF THIS WORK WITH THE WORK OF OTHER TRADES, AND FULL COMPLIANCE WITH THE CONTRACT DOCUMENTS.

By: John Currin

Company: RS&H
